

## AQ25742B Expansion Zoning Panel for 4 Valves

System commissioning date: \_\_\_\_\_

Customer: \_\_\_\_\_

Building address: \_\_\_\_\_

### INSTALLATION JOB RECORD

### INSTRUCTIONS:

Fill in the details of the equipment connected to the zoning module:

- A** Low voltage thermostats
- B** Low voltage zone valves without end switches
- C** Review and set DIP switch settings -once the DIP switches have been set, complete the "Installer settings" diagram by filling in the circles to indicate the DIP switch position

File this with other installation records for equipment used on this installation.


### A Zoning Thermostats

Terminal #	5-6	7-8	9-10	11-12
Terminal ID	TH1	TH2	TH3	TH4
Function	Zone call for heat			
Equipment				
Manufacturer				
Model #				
Date Code				
Notes				

### C Zoning Module DIP Switch Settings


DIP No.	Description
<b>1</b>	<b>Zone Address</b>
<b>2</b>	(Slide the DIP switch to the right position to indicate which group of zones this is; should be set to "1-4" for the first 4 space heating zones in the system [usually included with an AQ250 or AQ251 control panel], then "5-8" for the next group of 4 zones and so on. For each group of 4 zones, there can be only <u>one</u> DIP switch in the right hand position.)
<b>3</b>	
<b>4</b>	
<b>5</b>	<ul style="list-style-type: none"> <li>• If set to SYNC, zone synchronization is enabled.</li> <li>• If set to NOT, zone synchronization is disabled.</li> </ul>
<b>6</b>	<ul style="list-style-type: none"> <li>• If zone valves are normally closed (N.C.), set the NC/NO DIP switch to the OFF position.</li> <li>• If zone valves are normally open (N.O.), set the NC/NO DIP switch to the ON position.</li> </ul>
<b>7</b>	<ul style="list-style-type: none"> <li>• If set to Group (ON position) the zone outputs are energized with the AUX pump*.</li> <li>• If set to - (OFF position), the AUX Pump contacts are not affected by activity on these zones.</li> </ul>
<b>8</b>	<ul style="list-style-type: none"> <li>• If set to 2-Stg (ON position), then 2-stage operation is activated on thermostat inputs. The zoning module operates as two 2-stage zones or 3 zones (one 2-stage and two 1-stage).</li> <li>• If set to 1-Stg (OFF position), then operates as four 1-stage zones.</li> </ul>

\* If used with AQ250 RelayPlus Control Panel, the AQ15000B Boiler Control Module DIP switch #5 must be set to "GROUP" position and DIP switch #6 must be set to "MAIN" position  
 If used with AQ251 Boiler Reset Control Panel, the EQUIPMENT SETUP > AUXILIARY I/O > AUX PUMP menu option on the AQ251 must be set to "GROUP"

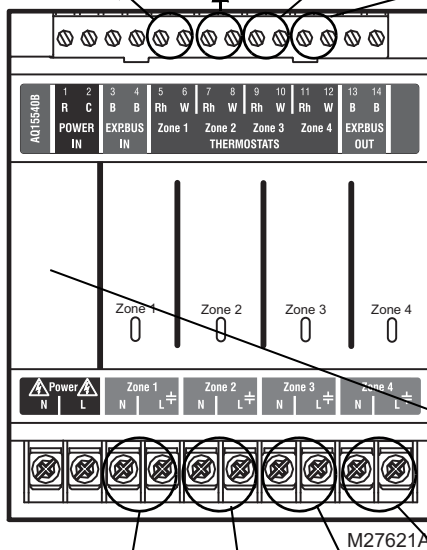



### B Zoning Valves

Terminal ID	Zone 1	Zone 2	Zone 3	Zone 4
System Zone #				
Function	Zone control			
Equipment	Valve	Valve	Valve	Valve
Manufacturer				
Model #				
Date Code				
Power draw VA				
Notes				




#### Factory Setting

#### Installer Setting



Fill in the circle to indicate position of DIP switch.



**Automation and Control Solutions**

Honeywell International Inc.  
1985 Douglas Drive North  
Golden Valley, MN 55422  
[customer.honeywell.com](http://customer.honeywell.com)

© U.S. Registered Trademark  
© 2013 Honeywell International Inc.  
69-2034—05 L.L. Rev. 10-13  
Printed in United States

**Honeywell**
